

Date Mon 08/12/2024

Job #

Prepared By Bradley Bender



Weather

6:00 AM

53° 

Clear

Wind: 0 MPH | Precipitation: .0" | Humidity: 100%

12:00 PM

75° 

Clear

Wind: 5 MPH | Precipitation: .0" | Humidity: 55%

4:00 PM

79° 

Partially cloudy

Wind: 3 MPH | Precipitation: .0" | Humidity: 43%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 8.00 am on site.

Topsoil pile removed Friday prior, 19 truck loads.

Randy and crew starting at soccer field, continuing to west in front of play ground, and intend to turn south to overlook.

Clarified with Colby at FPBH that type v subgrade is 3 inch agg, for a total of 6 inch under asphalt. Also need design profile spot grades on sheet c114 to establish grade and Benches.

Will need to review line and grade at turn behind water tower, as backslope may be into tower fence and legs.

10:00 am

Looked at staking for restroom and parking at commons. Grades for parking area make no sense (2 and 3 foot cut), but no grades on plans so will field adjust.

11:30 am

Forwarded revised sheet c-114 to Randy and others, stopped by to see they had started on the T line to the overlook. Randy stated existing grade off by over a foot.

3:00 pm

Stopped at T line to overlook. Randy to have ILS check grades. Lots of debris and large holes in the area, probably from school demo used to enlarge parking lot. Advised to tape area off to keep public out.

Bradley Bender | 08/12/24 | 03:17PM

Site Safety Observations

No entry


Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Attachments

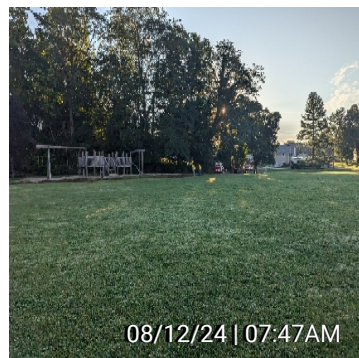



BBB

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 08/12/24 | 03:22PM
