

Vernon Trail NLT-0208

Bender Projects

65 South Street Vernon, Indiana 47282

Date Fri 08/23/2024

Job #

Prepared By Bradley Bender



Weather

6:00 AM

51°

Partially cloudy

Wind: 1 MPH | Precipitation: .0" | Humidity: 96%

12:00 PM

74°

Clear

Wind: 5 MPH | Precipitation: .0" | Humidity: 48%

4:00 PM

83°

Clear

Wind: 2 MPH | Precipitation: .0" | Humidity: 41%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 9.00am

Randy planning to stone, north end may need 30 foot more retaining wall to the north. He will add millings, but leave open for other concrete crew.

Advised to check for roots at current grade, and saw back those in slopes.

Also discussed existing stone, removed and placed behind house for reset. Requested parking single axle dump truck away from gym, possibly off pike Street at soccer trail.

9.45am

Spoke with David Boswell regarding lists and logs, extra wall. Documents to arrive early next week. Plan for progress meeting next Wednesday at commons.

Bradley Bender | 08/23/24 | 09:47AM

Site Safety Observations

No entry


Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Attachments

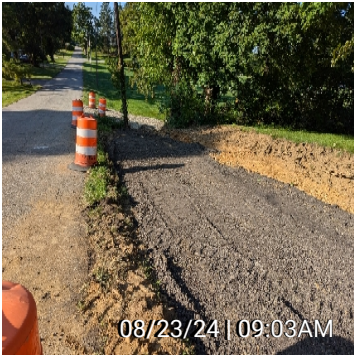

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 08/23/24 | 09:47AM
