

# Vernon Trail NLT-0208

Bender Projects

65 South Street Vernon, Indiana 47282

Date Tue 09/10/2024

Job #

Prepared By Bradley Bender



## Weather

6:00 AM

48°

Partially cloudy

Wind: 1 MPH | Precipitation: .0" | Humidity: 96%

12:00 PM

76°

Clear

Wind: 4 MPH | Precipitation: .0" | Humidity: 40%

4:00 PM

82°

Clear

Wind: 4 MPH | Precipitation: .0" | Humidity: 28%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

### 1. 9.00am

Crew setting up for excavating footer for pike street retaining wall and added 30 lft, per revised detail. Still no pricing for the extra from David Boswell.

12.30pm

Footer and agg bedding nearly complete. Reviewed West Jackson work with Randy, set up appointment with Steele Myers for next day to look at added drives. Crew moved to rear of school lot for parking and trail, and green area. Filed survey of topography behind existing shelter and water tower for retaining wall alignment and grade changes.

Bradley Bender | 09/11/24 | 08:09AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey



Questions

N/A No Yes Description

1. Any accidents on site today?

2. Any schedule delays occur?


3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

Attachments

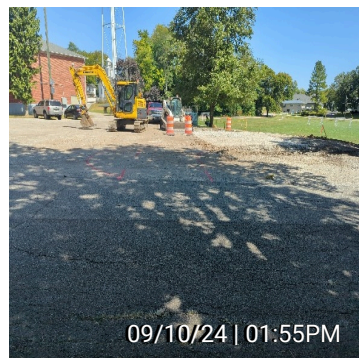

*BfBe*

---

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 09/11/24 | 08:09AM
