

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Wed 12/04/2024

Job #

Prepared By Bradley Bender



Weather

6:00 AM

26°

Overcast

Wind: 11 MPH | Precipitation: .0" | Humidity: 84%

12:00 PM

43°

Overcast

Wind: 22 MPH | Precipitation: .0" | Humidity: 54%

4:00 PM

46°

Partially cloudy

Wind: 13 MPH | Precipitation: .0" | Humidity: 62%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. On site 8.00am to 11.00 am, assisted in continuing to lay out ramps and bollards and drives for saw cut and excavation for concrete crew expected Friday or Monday.
Montgomery and Washington met plan and spec for ada grade.

Added 20 foot wide drive on Montgomery from allowance for alley and garage where cars crossed trail.

Drives at east jackson, ramp at posey meet plan and spec, east ramp at posey has 10% cross slope at roadway. May need to hold panel domes back for transition slope.

Ramp at jackson at west side commons enlarged to 25 feet in length to overcome paving irregularities. Ok per contractor as it is on them. Very shallow gas, bollard may be an issue.

East side meets plan and spec.

1.00pm to 2.00pm

Call from Jon French of Rohe, asking to meet regarding tree removal on unimproved portion. Met in 15 minutes on site, hiked to show downed trees. They will text when doing the work in the next few weeks, will cut to 4 foot lengths and roll down below.

6.30pm

Met with scoutmasters Josh Shaw and Dave Shaw regarding boy scout volunteer work for unimproved

section. They will plan a Saturday for local troop to help define the corridor, then can schedule for larger groups to perform more clearing.

Bradley Bender | 12/05/24 | 05:18AM

Site Safety Observations

No entry

Quality Control Observations




No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments



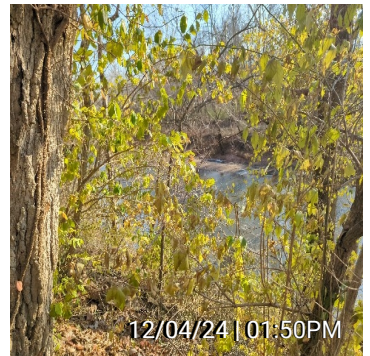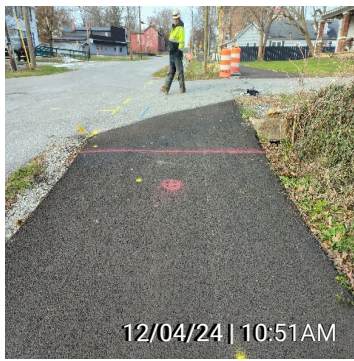

Bradley Bender

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 12/04/24 | 07:46PM
