

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Tue 12/10/2024

Job #

Prepared By Bradley Bender



Weather

6:00 AM

43° 

Overcast

Wind: 1 MPH | Precipitation: .0" | Humidity: 97%

12:00 PM

46° 

Rain, Overcast

Wind: 5 MPH | Precipitation: .01" | Humidity: 96%

4:00 PM

46° 

Partially cloudy

Wind: 8 MPH | Precipitation: .0" | Humidity: 84%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 9.30am

Concrete pour canceled, crew to form across from overlook and drive on Montgomery. Trail at overlook to be saw cut again to give more for bollard standard detail.

Bradley Bender | 12/10/24 | 10:07AM

2. 2.00pm to 3.00pm

Concrete crew left early during sprinkles. Worked with excavation crew to move restroom east about 8 feet to be about 5 feet off the force main, and rotated slightly northwest to avoid most of tree drip edge. Force main under prior west side of restroom only just over about 3 feet deep.

Shot spot grades for tie in of walk at trail to verify finish floor, may need some adjustment now as at 3% instead of 2%.

Also took spot shots at shelter and parking in order to fix drainage and prepare ada access to shelter, as asphalt enters at 7.7% with valley and crown.

Bradley Bender | 12/10/24 | 04:08PM

Site Safety Observations

No entry


Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments

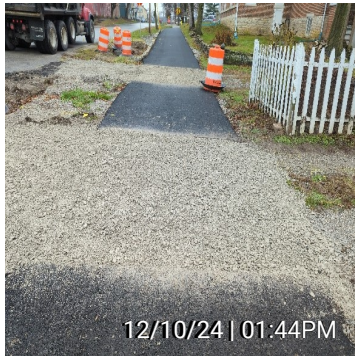

BfBe

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 12/11/24 | 09:50AM
