

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Fri 12/13/2024

Job #

Prepared By Bradley Bender



Weather

6:00 AM

22° 

Partially cloudy

Wind: 9 MPH | Precipitation: .0" | Humidity: 83%

12:00 PM

31° 

Clear

Wind: 7 MPH | Precipitation: .0" | Humidity: 63%

4:00 PM

35° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 59%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 8.30am

Alley crossing at pike formed, waiting on mix. Excavation crew working between soccer restroom and gym.

12.30pm

Layed out slab attachments for access to trail and fountain, and trail access to existing shelter. Can not connect to ramp to wall as too steep. Took slab from 16 x 16 to 15 x 15 to swap for access panels and deduct for water line crossing ramp. Pour building to building and form curb on low end at gym.

1.15 pm

Met with mayor wayne zamora and jeff walker. Reviewed trail through gym to slab. They like to see gates changed to block vehicles from crossing trail, along south side of drive and ramps. Approved of slab and fountain and shelter access. Reviewed overlook and recommended wheelstops as part of trailhead and safety improvements.

Requested I continue to contact matt owens regarding his walk connection to trail and grouting of utility connection.

Bradley Bender | 12/13/24 | 03:29PM



Site Safety Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments

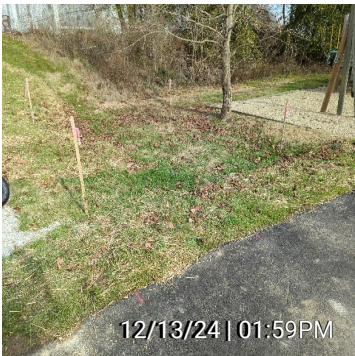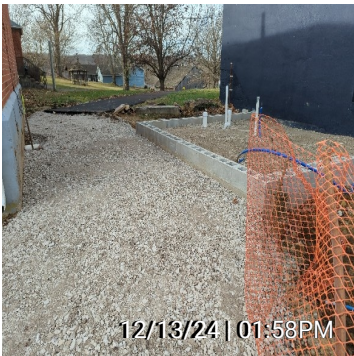

BfB

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 12/13/24 | 03:29PM
