

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Thu 12/19/2024

Job #

Prepared By Bradley Bender



Weather

6:00 AM

31°

Overcast

Wind: 0 MPH | Precipitation: .0" | Humidity: 90%

12:00 PM

34°

Overcast

Wind: 6 MPH | Precipitation: .0" | Humidity: 79%

4:00 PM

38°

Partially cloudy

Wind: 8 MPH | Precipitation: .0" | Humidity: 75%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 8.30am

Crews at soccer wall, removed existing forms as grade was not matching, and attempting to set new chalklines. Part of footer within limits. Finding that previous chalklines set by degrees not percentage. To be reviewed at 10.00 am meeting.

10.00am to 11.30am No pictures taken

Large group meeting, Scott Dawson, Jay Gerth, zach hicks, david Boswell, jeff poole, concrete crew and excavation crew, Colby king and chris from fpbh. Announced that the combination of existing and construction problems were making it difficult for compliance and need for direction to proceed. Reviewed posey and jackson, wedge and level and chase of slopes. Reviewed 2 drive crossing at mid block. Reviewed commons parking and ada access to shelter. Moved to soccer wall. In all cases omara superiors committed to tear out as needed so that new can be installed correctly, and to avoid patches. Handrail will be needed now on both sides of wall ramps, price to be submitted. Crews will be off until January 2 or so, but footers for restroom may be sooner.

1.30pm


Crew chipping out footer thst is too high, laying out lower end for tie in. Established 9 foot widrh so that rsil has mounting options for 8 foot clear. David checking with suppliers that provide shop drawing and wall mounts.

Bradley Bender | 12/19/24 | 03:45PM

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments

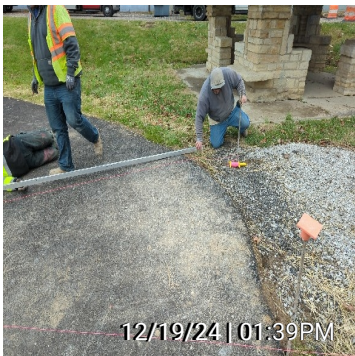

Bradley Bender

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 12/20/24 | 09:02AM
