

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Tue 02/04/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

36° 

Overcast

Wind: 13 MPH | Precipitation: .0" | Humidity: 91%

12:00 PM

39° 

Partially cloudy

Wind: 9 MPH | Precipitation: .0" | Humidity: 63%

4:00 PM

44° 

Clear

Wind: 2 MPH | Precipitation: .0" | Humidity: 53%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 7.45am

Concrete crew onsite at school lot, planning to work on forming slab at retaining wall.

12.45pm

Crew resetting forms to match 9 foot 6 inches width to accommodate stone and handrail. As currently set, west end straight grade into footer. Level landing brought up, then 8 percent to west, then 3 percent to drive, just Skims over footer that was placed too shallow. Footer removal not allowed.

Lower end brought up for Transition panel at west side existing asphalt. Part of capstone will be below slab.

I am letting them pour a little thinner, and right on top of part of the footer. This will also allow the hand rail to be shorter, some dowels or reinforcement needed over footer.

Bradley Bender | 02/04/25 | 06:18PM

Site Safety Observations

No entry


Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments

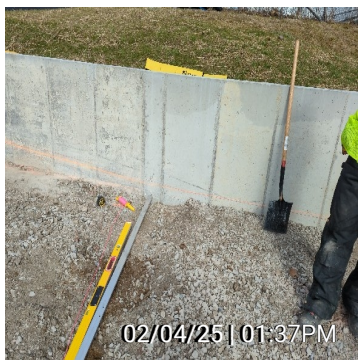

BfB

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 02/06/25 | 04:38PM
