

# Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Wed 02/05/2025

Job #

Prepared By Bradley Bender



## Weather

6:00 AM

31° 

Overcast

Wind: 12 MPH | Precipitation: .0" | Humidity: 86%

12:00 PM

35° 

Overcast

Wind: 11 MPH | Precipitation: .0" | Humidity: 65%

4:00 PM

33° 

Rain, Overcast

Wind: 12 MPH | Precipitation: .07" | Humidity: 85%

## Work Logs

No entry

| Name  | Description | Quantity | Total Hours |
|-------|-------------|----------|-------------|
| Total |             | 0        | 0           |

## General Notes

### 1. 8.30am

Form set for slab off wall. Concrete available, crew to pour all at 9.00am. Exc crew laying out to west.

10.00am

Assisted with layout from door of new rest room, to western tie in, along gym wall, and for drive crossing. Layed out new slab grades and tie for picnic slab. Discussed rough in for fountain and hydrant.

12.30pm

Hiked to water street and on, to mark pedestrian bridge crossing, and verify removal by rohe on unimproved trail.

1.30pm

Informed that it appears the reason that asphalt trail cross slope is off may have been smart level in degrees instead of percent.

Inspected soccer restroom, poor flashing, 2 90s outside wall, etc.

Went under gym to check saddle backfill. No backfill support under pipe, pipe capped, still to be run west to tie to cast iron. Opened manhole and dyed to see where school runs, to see if they could have connected differently.




Bradley Bender | 02/06/25 | 04:39PM

## Survey

| Questions                             | N/A                                 | No                       | Yes                      | Description |
|---------------------------------------|-------------------------------------|--------------------------|--------------------------|-------------|
| 1. Any accidents on site today?       | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 2. Any schedule delays occur?         | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 3. Did weather cause any delays?      | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 4. Any visitors on site?              | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 5. Any areas that can't be worked on? | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 6. Any equipment rented on site?      | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |

## Attachments



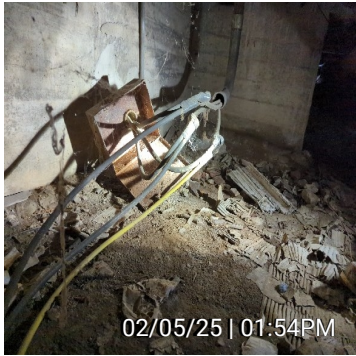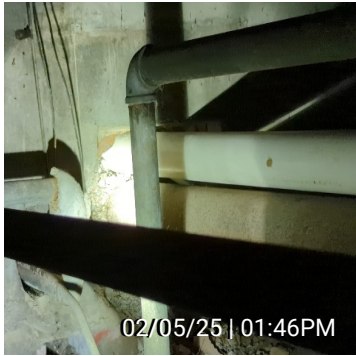



*ByBBe*

---

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 02/06/25 | 04:39PM
