

# Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Thu 02/06/2025

Job #

Prepared By Bradley Bender



## Weather

6:00 AM

40° 

Rain, Overcast

Wind: 5 MPH | Precipitation: .01" | Humidity: 98%

12:00 PM

43° 

Overcast

Wind: 10 MPH | Precipitation: .0" | Humidity: 88%

4:00 PM

38° 

Overcast

Wind: 10 MPH | Precipitation: .0" | Humidity: 84%

## Work Logs

No entry

| Name  | Description | Quantity | Total Hours |
|-------|-------------|----------|-------------|
| Total |             | 0        | 0           |

## General Notes

### 1. 9.00am

Met with David Boswell to discuss less rail, and exc crew needed fountain and hydrant for rough in, as the lower water service and reroute underdrain.

Koch crew at commons roughing for underslab.

Concrete crew prepping to pour at commons, posey, and ramps at west end of wall.

### 2.00pm

David on site, may have different rail supplier. Discussed needing to check forms by soccer restroom before pour.

Met with Wayne and amber reviewed soccer restroom, and discussed yrail progressand features.

### 3.00pm

Concrete crew at jackson commons west of commons, panels as proposed extended into street. Approved less panel, saw cut more at edge, maintain 8 foot.


Checked forms at west side wall and soccer restroom. Needed to adjust run about an inch to be under 5 percent, and then match existing drive crossing can be around 6 percent.

Bradley Bender | 02/06/25 | 04:53PM

## Survey

| Questions                             | N/A                                 | No                       | Yes                      | Description |
|---------------------------------------|-------------------------------------|--------------------------|--------------------------|-------------|
| 1. Any accidents on site today?       | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 2. Any schedule delays occur?         | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 3. Did weather cause any delays?      | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 4. Any visitors on site?              | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 5. Any areas that can't be worked on? | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |
| 6. Any equipment rented on site?      | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |             |

## Attachments

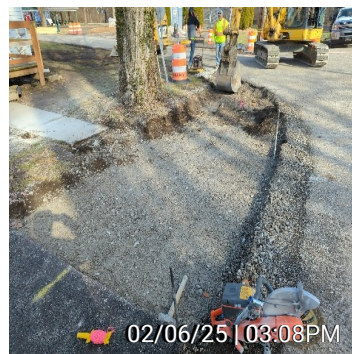



*Bradley Bender*

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 02/06/25 | 04:55PM
