

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Thu 02/13/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

30°

Overcast

Wind: 14 MPH | Precipitation: .0" | Humidity: 85%

12:00 PM

29°

Overcast

Wind: 14 MPH | Precipitation: .0" | Humidity: 71%

4:00 PM

27°

Overcast

Wind: 13 MPH | Precipitation: .0" | Humidity: 78%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 8.30am

Neither crew on site prior day due to weather and safety meetings.

Concrete crew preparing to pour at east side jackson and posey. No bollard width due to gas line.

Plan to pour perry and jackson later today, mid jackson drives friday. No work planned for them next week due to predicted extreme cold.

Exc crew prepping Perry and jackson, will install underdrain at end of existing concrete pipe to daylight. Not removing as much asphalt, conc to make transition.

Exc crew will probably work on commons utilities next week.

2.00pm

Concrete crew went ahead with mid block drives, will form and pour perry tomorrow. Road edge at alley may need saw cut due to jagged appearance.

Exc crew placing stone backfill at drive crossing at soccer wall.

Bradley Bender | 02/13/25 | 04:01PM

Site Safety Observations

No entry

Quality Control Observations


No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments



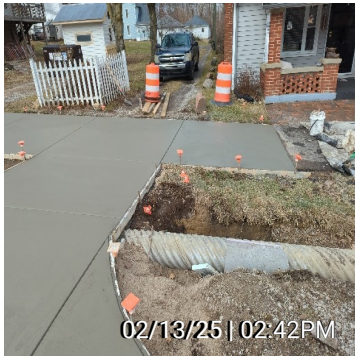

BfB

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 02/13/25 | 04:03PM
