

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Mon 03/03/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

26° 

Clear

Wind: 2 MPH | Precipitation: .0" | Humidity: 79%

12:00 PM

38° 

Overcast

Wind: 11 MPH | Precipitation: .0" | Humidity: 41%

4:00 PM

47° 

Partially cloudy

Wind: 11 MPH | Precipitation: .0" | Humidity: 30%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 7:30 am

Informed exc crew and Dakota of 5 various areas with conflicts between plan and filed to be resolved. Water Street trailhead, Pedestrian Bridge, Pike Highway intersection, Overlook, and Stone column sign. Many subsequent phone calls with David Boswell.

Exc crew installing new pipe across Poplar, concrete crew removing forms from behind restroom, and Jackson Street drives, resetting bricks at courthouse. Poole crew at Pike street wall.

1:00pm

Concrete crew out for the rest of the day.

Pipe at Poplar 50% complete, road to be opened around 3:30pm.

Bradley Bender | 03/05/25 | 06:35AM

Site Safety Observations

No entry


Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments

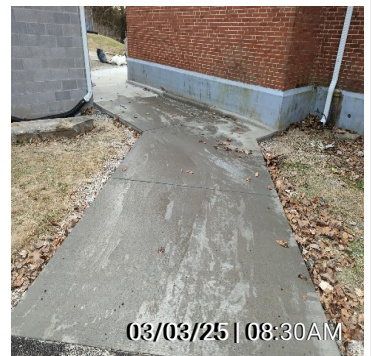



Bradley Bender

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 03/05/25 | 06:35AM
