

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Mon 03/10/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

34° 

Clear

Wind: 2 MPH | Precipitation: .0" | Humidity: 79%

12:00 PM

57° 

Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 32%

4:00 PM

66° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 22%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- 8.30am
Call from dakota, mcclure crew replaced by Hensley crew. Plan to add fill and pour walk at water street trailhead, and exc crew can backfill and add riorap at ped bridge.
9.00am
New crew removing netting at soccer field, water street being prepped.
10.30am
Met exc crew at soccer field, explained practice starting this evening, need to make some room. Discussed hydrant and fountain and winterization pit.
1.00pm
Met cody and Hensley at pike and highway to review for tear out, on to Montgomery and highway and next alley crossing. Will check on fiber optic box, and plan appears to have panels at alley.
Looked st riprap at ped bridge, used twice the quantity authorized. Danny went over sill at bridge approach. Reviewed samples for cap stone from poole phone call. No one from poole on site at commons.

Bradley Bender | 03/10/25 | 04:22PM

Site Safety Observations

No entry

Quality Control Observations






No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments



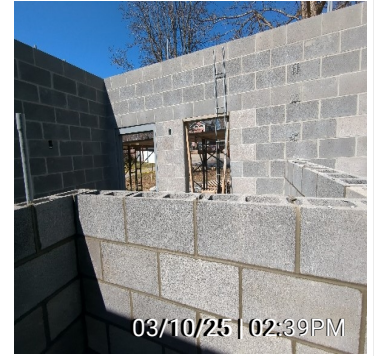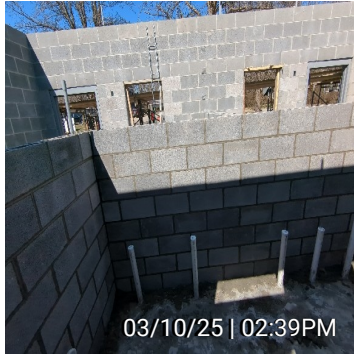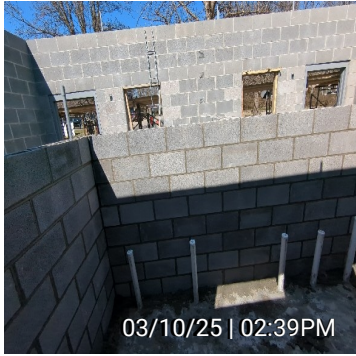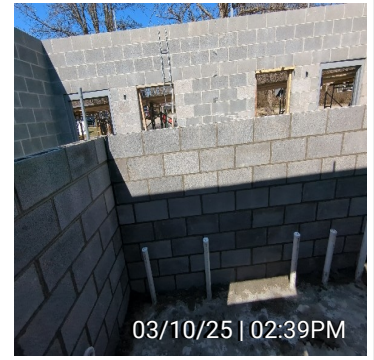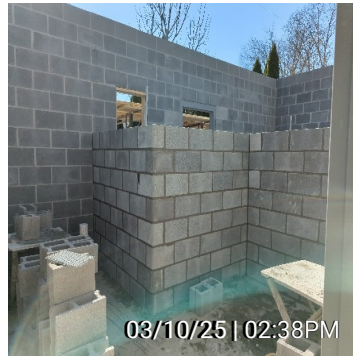

Bradley Bender

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 03/16/25 | 06:16AM
