

Vernon Trail NLT-0208

Bender Projects

65 South Street Vernon, Indiana 47282

Date Thu 03/13/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

41°



Clear

Wind: 5 MPH | Precipitation: .0" | Humidity: 86%

12:00 PM

63°



Clear

Wind: 8 MPH | Precipitation: .0" | Humidity: 45%

4:00 PM

76°



Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 29%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- 8:00am
Bridge site, 2nd conc crew poured deadman / sill prior day, planning to finish Friday. Conc crew formed curb at Pike and highway for 10:00 am pour.
10:00 am
Poured Curb, starting prep for ramps and walk, had removed more asphalt for tie in, still non compliant.
Noon
Soccer restroom being finished by others. Tying walk to trail.
Bradley Bender | 03/16/25 | 06:27AM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions

N/A No Yes Description

1. Any accidents on site today?

☒ ☐ ☐

2. Any schedule delays occur?

☒ ☐ ☐

3. Did weather cause any delays?

☒ ☐ ☐

4. Any visitors on site?

☒ ☐ ☐


5. Any areas that can't be worked on?

☒ ☐ ☐

6. Any equipment rented on site?

☒ ☐ ☐

Attachments

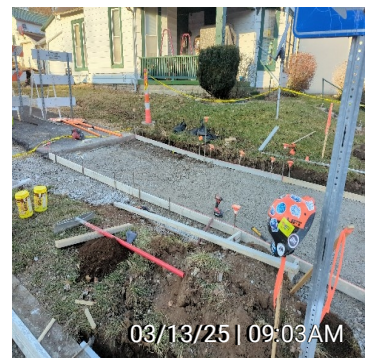



BfBe

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 03/16/25 | 06:27AM
