

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Fri 03/14/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

50° 

Clear

Wind: 4 MPH | Precipitation: .0" | Humidity: 81%

12:00 PM

70° 

Clear

Wind: 14 MPH | Precipitation: .0" | Humidity: 53%

4:00 PM

76° 

Partially cloudy

Wind: 18 MPH | Precipitation: .0" | Humidity: 46%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- 11.00 am
Part of walk ramp at Pike Highway poured prior afternoon, remainder completed in morning. Poole group setting trusses at restroom. Afternoon to be spent with all crews, on placing topsoil, cold patch, various site cleanup, removing barrels etc.
Plan on Monday to set fountain, pour slab at soccer area, and connector to water street kiosk, then concrete crew will move out.

Bradley Bender | 03/16/25 | 06:34AM

Site Safety Observations

No entry

Quality Control Observations


No entry

Survey

Questions	N/A	No	Yes	Description
-----------	-----	----	-----	-------------

1. Any accidents on site today? ☒ ☐ ☐
2. Any schedule delays occur? ☒ ☐ ☐
3. Did weather cause any delays? ☒ ☐ ☐
4. Any visitors on site? ☒ ☐ ☐
5. Any areas that can't be worked on? ☒ ☐ ☐
6. Any equipment rented on site? ☒ ☐ ☐

Attachments

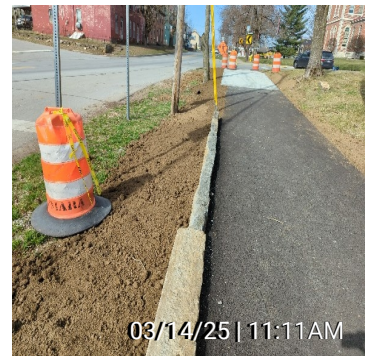

BfBe

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 03/16/25 | 06:53AM
