

# Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Mon 03/17/2025

Job #

Prepared By Bradley Bender



## Weather

6:00 AM

33° 

Partially cloudy

Wind: 6 MPH | Precipitation: .0" | Humidity: 86%

12:00 PM

40° 

Clear

Wind: 1 MPH | Precipitation: .0" | Humidity: 58%

4:00 PM

49° 

Clear

Wind: 8 MPH | Precipitation: .0" | Humidity: 45%

## Work Logs

No entry

| Name  | Description | Quantity | Total Hours |
|-------|-------------|----------|-------------|
| Total |             | 0        | 0           |

## General Notes

### 1. 8.00am

Exc crew with out Steve Hensley setting up to place fountain so slab can be formed for 1.00pm pour. Assisted with layout and direction. Concrete crew forming last walk at water street. Walked all site to observe after 4 inch weekend rain. Only issues are on Jackson from poplar to water, exposed aggregate disturbed, especially at alley.

Poole carpenters at restroom. Flagman ahead signs on highway for later in the day.

### 11.00 am

Crew won't make 1.00pm pour, discussed overtime or Tuesday with shop. Plan for Wednesday. Steve will place 6 inch sleeve for fountain and set anchors later. Will begin clearing at overlook.

### 3.00pm

Some overlook clearing remains, forms in place. All crews gone for Tuesday, return Wednesday.

Bradley Bender | 03/17/25 | 05:09PM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

### Questions

1. Any accidents on site today?



2. Any schedule delays occur?



3. Did weather cause any delays?



4. Any visitors on site?



5. Any areas that can't be worked on?




6. Any equipment rented on site?



## Attachments



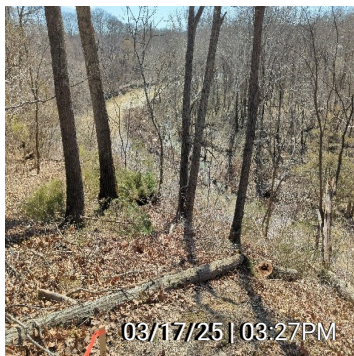



*BfB*

---

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 03/17/25 | 05:10PM
