

Date Wed 09/04/2024

Job #

Prepared By Bradley Bender



Weather

6:00 AM

52° 

Clear

Wind: 2 MPH | Precipitation: .0" | Humidity: 91%

12:00 PM

73° 

Clear

Wind: 3 MPH | Precipitation: .0" | Humidity: 59%

4:00 PM

84° 

Clear

Wind: 2 MPH | Precipitation: .0" | Humidity: 44%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 9.30am

Crew has commons to posey open and ready for stone.

Gas crew on site at east end repairing leaking connections. All gas very shallow, gas has no plans to lower or relocate.

Existing water meter at tre removal about 2 inch high for grade, no need to lower, adjust grade to match.

Proposed pipe at posey can not be placed as outfall would be into gas line, and also outfall would end up 12 inch or more below trail and pavement, leaving vertical edges between the two.

Recommend cleaning existing pipe to verify condition, headwalls to remain, then collar on new pipe out that could either daylight onto trail or be in subbase and outlet to ditch to east, north of trail.

Bradley Bender | 09/04/24 | 12:12PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions

N/A No Yes Description

1. Any accidents on site today?

2. Any schedule delays occur?


3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

Attachments

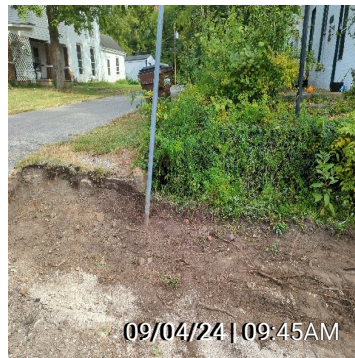

BBB

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 09/04/24 | 08:32PM
